


Ivalua Platform Phase 1: Quarterly Status

October 3, 2025

Agenda


- Project Overview
- Project Status
- Change Management Key Dates
- Change Management Communication Schedule
- High-Level Changes
- Next Steps

Project Overview

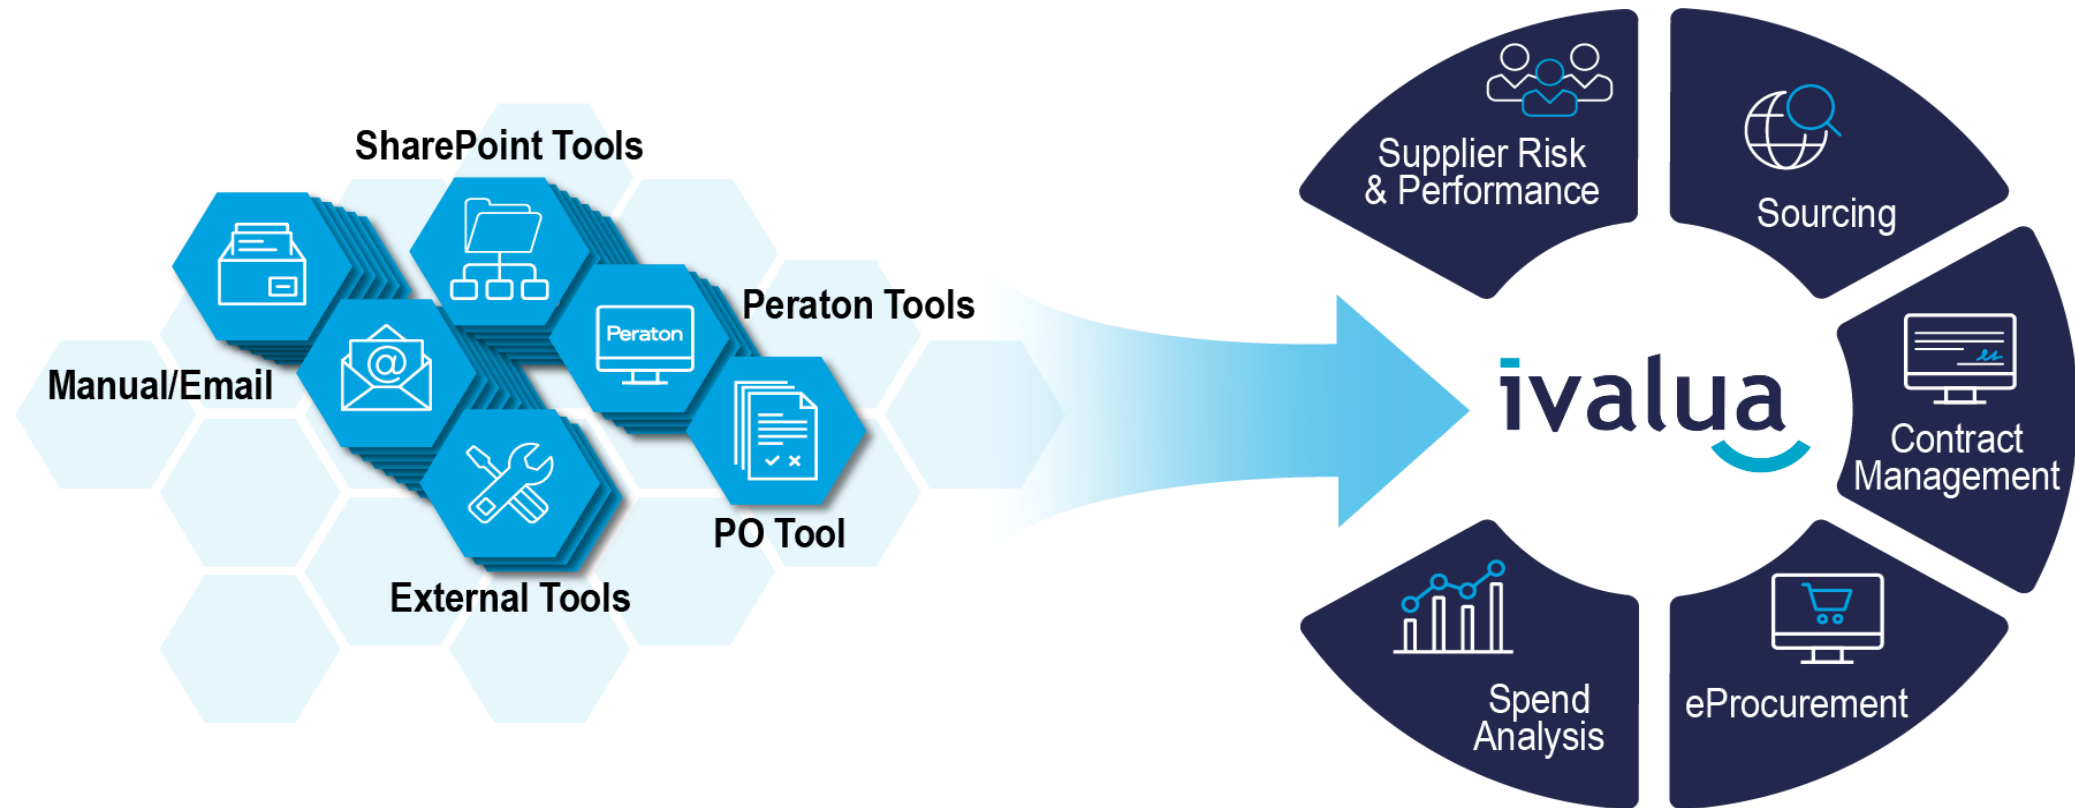


Implementing Ivalua marks a major step forward in **modernizing our procurement process**—giving us greater visibility, control, and efficiency across every transaction.

Scope

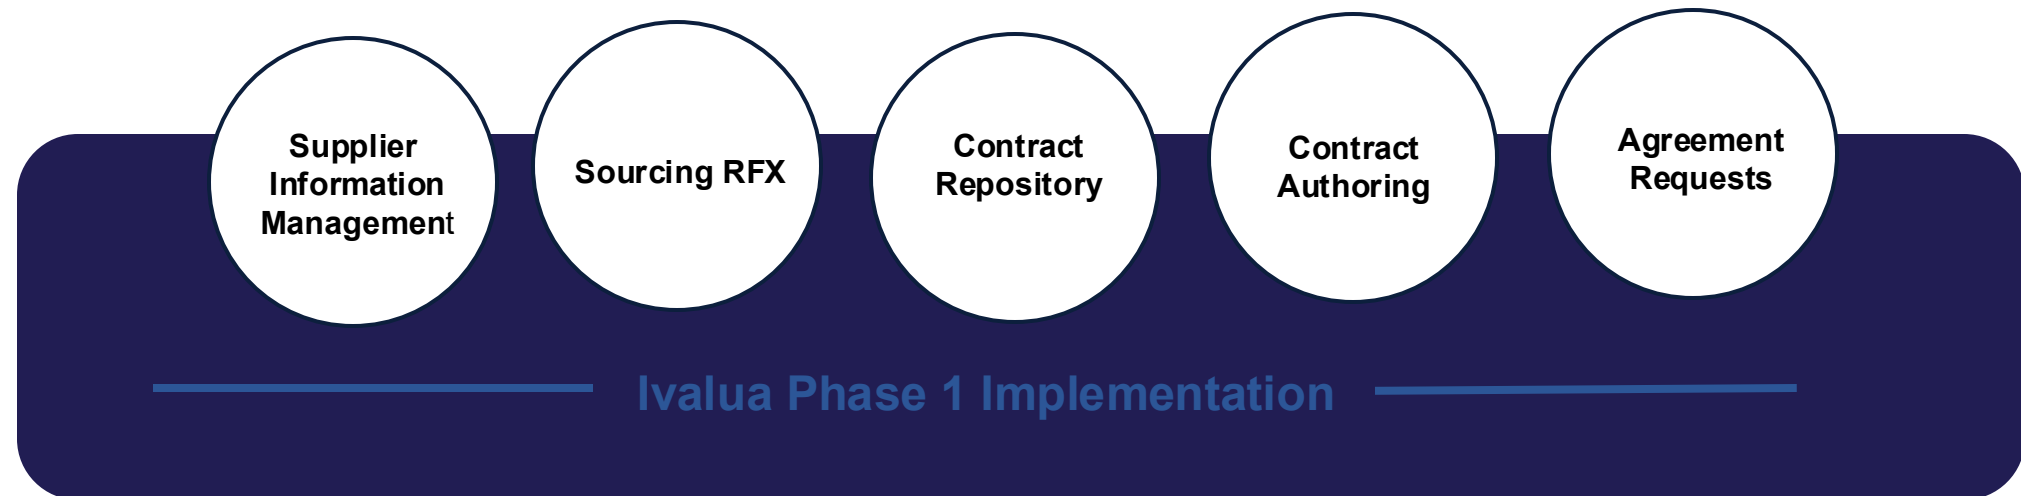

Project Timeline by Phase

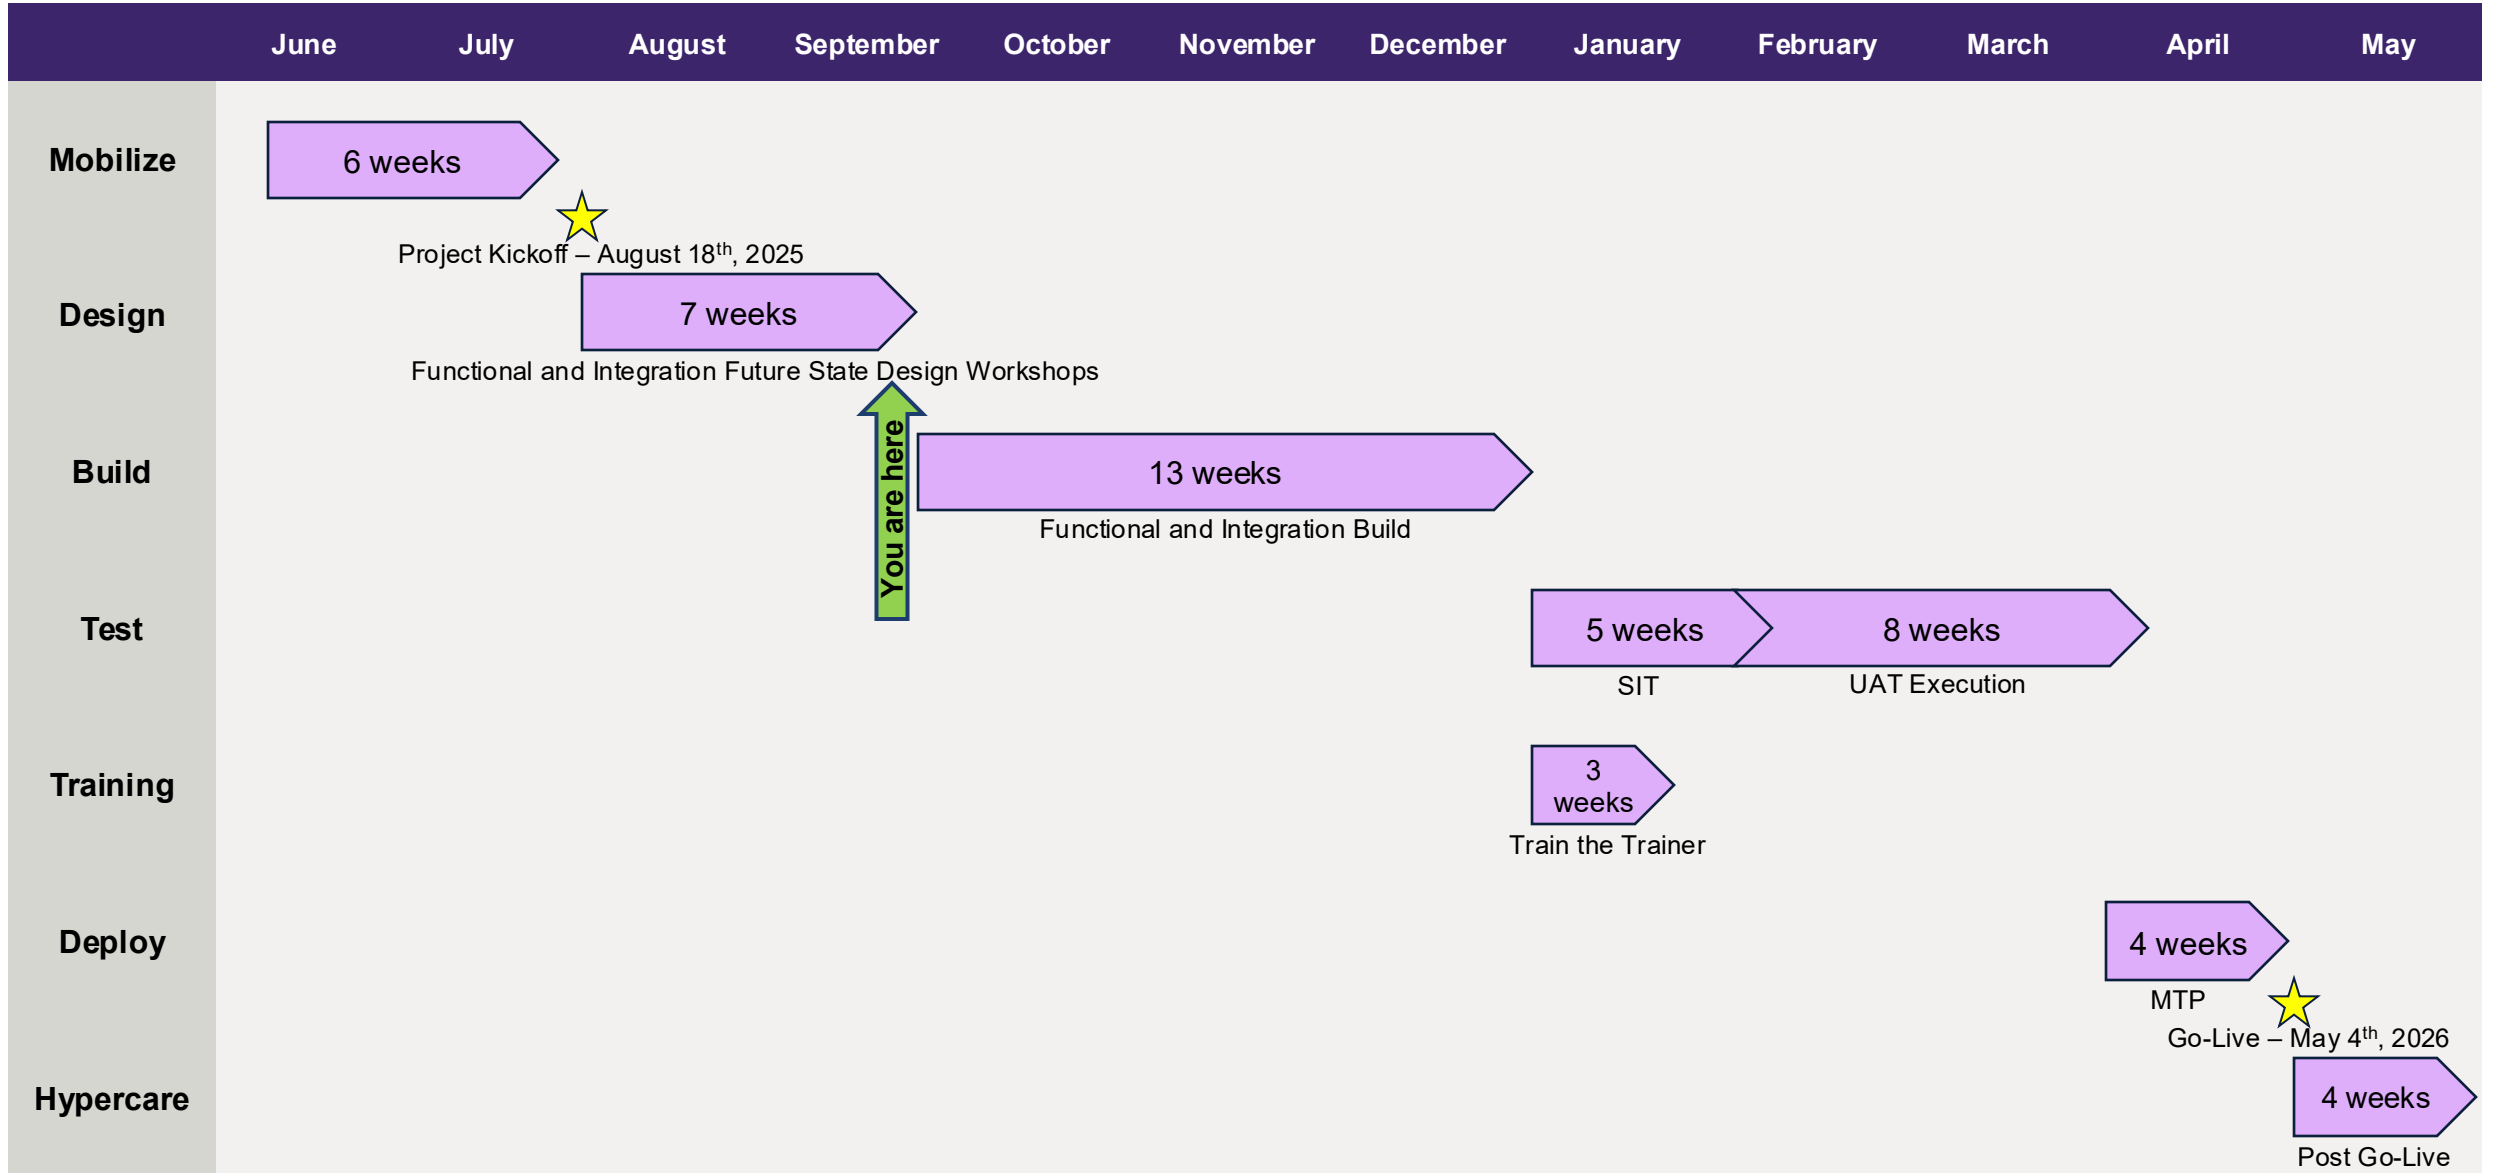

Phase 1: Ivalua Implementation Weekly Status

Current Status

- Project is 17% complete (week 7 of 41 weeks)
- Design 100 % complete (week 7 of 7 weeks)

Recent Accomplishments

- Documented designs are complete for each workstream and integration.

Known Changes

- See slide 10

Upcoming Activities

- Project team preparing to launch Build Phase – 10/06/2025
- Training team to wrap up training requirements – 10/10/2025
- Change management team continue to assess readiness and resistance – 10/10/2025

Communication Plan

Communication Type	Date	Method
Initial communication	09/5/2025	Email, Peraton Supplier Portal, Procurement LENSs, Peraton Weekly Newsletter
Weekly Status	09/15/2025	Email, Peraton Supplier Portal, Peraton Change Agent TEAMS channel
Quarterly Briefing	10/03/2025	Virtual
Design Briefing	11/07/2025	Virtual
UAT Announcement	12/05/2025	Email, Peraton Supplier Portal, Procurement LENSs, Peraton Weekly Newsletter
Build Demo	12/14/2025	Virtual
Training Announcement	02/16/2025	Email, Peraton Supplier Portal, Procurement LENSs, Peraton Weekly Newsletter
Go-Live & Post Support Readiness	03/05/2025	Virtual, Email, Peraton Supplier Portal, Procurement LENSs, Peraton Weekly Newsletter


Key Change Management Dates

Milestone	Start Date	End Date
UAT Training	1/5/26	2/6/26
UAT	2/9/26	4/3/26
Go-Live Readiness	3/5/26	3/27/26
Training	3/30/26	4/24/26
Deploy	05/04	



Phase 1 Implementation High Level Impact



Current State

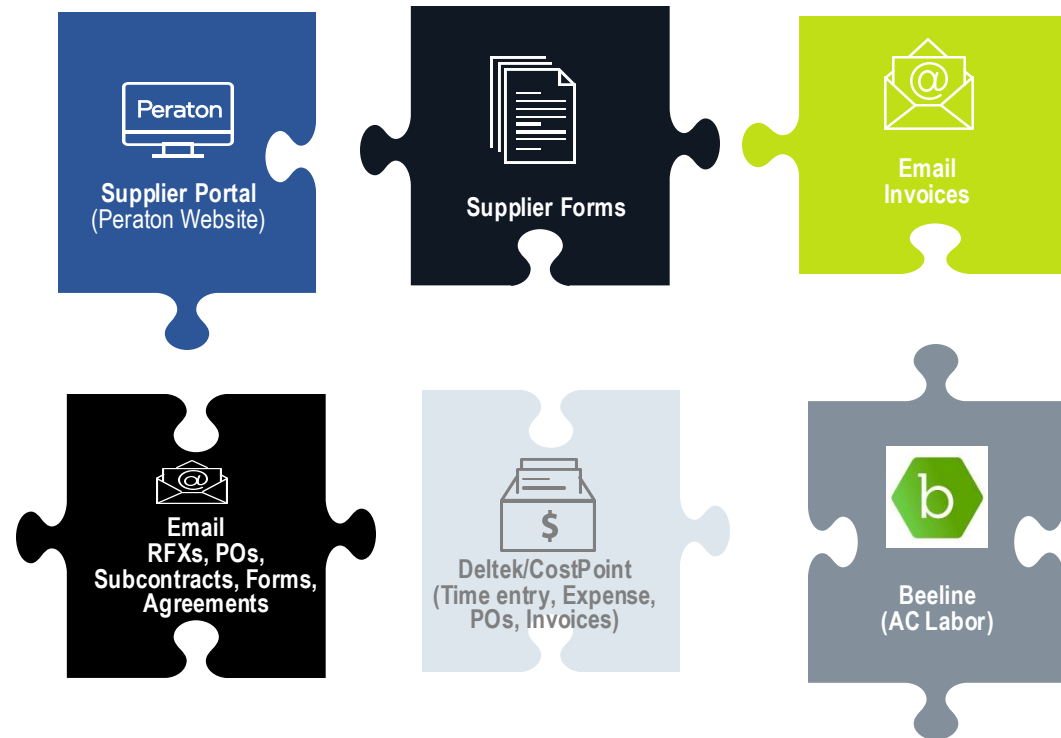

Future State

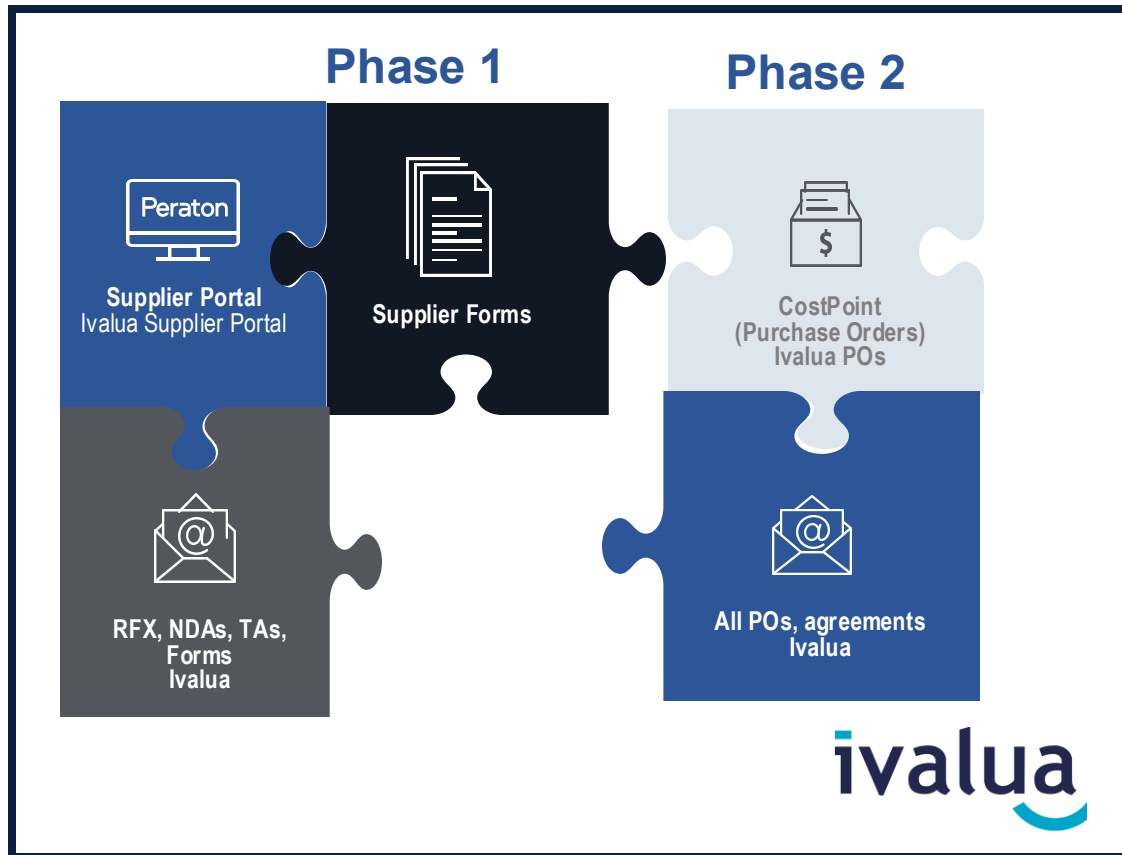

Wrap Up



Next Steps

- 1 Watch for updates on the Peraton website ([supplier portal](#)) or via email.
- 2 Submit questions to peratonprocurement@peraton.com.

Thank You

